

Grenfell Tower 3482

Progress Report No 1

14/7/2014

Progress Report No

Report on Progress up to Monday 14/7/2011

Contract Commencement : 2nd June 2014

Contract Completion : 5th June 2015

Contract Period : 53 weeks

Programme Week : 7

Progress Week :


Time to Contract Completion : 46

Inclement Weather to date : None

1.0 Progress:

Ramp:

Demolition is complete and the boundary agreed with Bouygues has been cleared and Hinesh (Bouygues) has been informed.

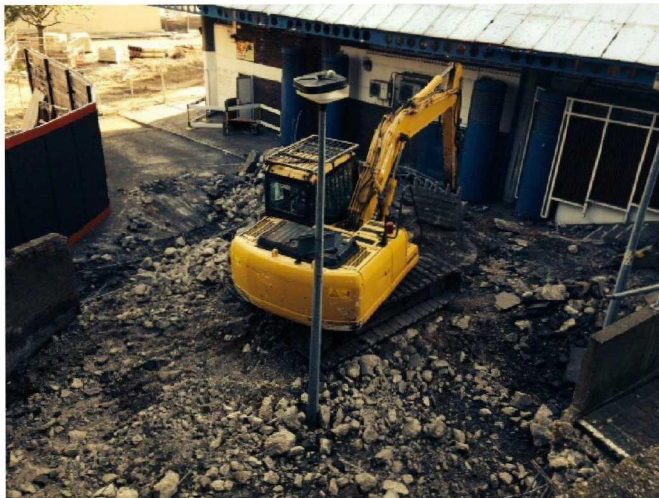

Canopy:

The canopy removal is underway with the west wing complete and large above ground ventilation ducts being removed as well.



Boxing Club re-location

The works to the temporary boxing club in Lowerwood court are progressing well and will be complete by Friday 18th July.

Cladding Mock up

The mock up of the proposed cladding system is now complete and available for comment on Walkway level outside the existing housing office.

4.1 Subcontract orders due in next period

Cladding Contractor
Access equipment
M+E Contractor

4.2 Health and Safety

1 visit in the period attached

5.0 Finance

JOB:

Financial Update		MAIN CONTRACT		All figures after retention		
Valuation No	Valuation Date	Agreed Cumulative Application	Agreed Net Application	Certificate Date	Payment Date	Payment Received
1						
2						
3						
4						
5						
6						
7						
8						
9						
10						
11						
12						
13						
14						
15						
16						

8.0 Information Required

Scope of works for CCTV survey
